Nural Pulse

KPI guide

Management overview. What the page shows and how to use it.

For Team leads and PM


NURALTECH · internal · Powered by Bitrix24 and Nural

21 October 2026

01 KPI

Management overview

The management overview of every project and department. Period: Day, Week or Month; "closed" and "on-time" compare with the period before.

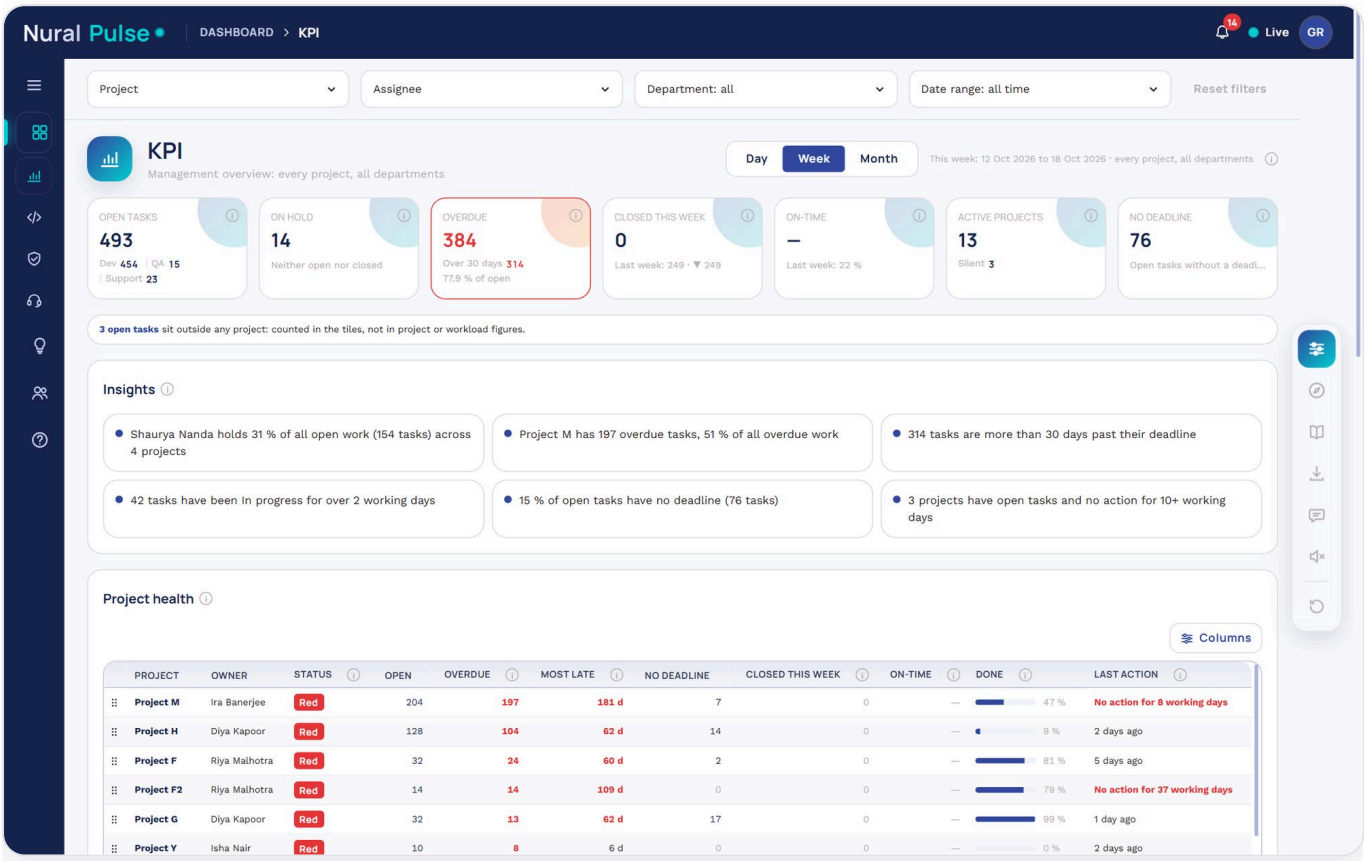

KPI, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Day, Week or Month	The period changes only the glowing data points: Closed, On-time, Project health (closed in the period) and People (delivered in the period), each compared with the period before. Open, On hold, Overdue, Projects and No deadline are counted as of now, whatever the period. Every task in every project, all departments. A task is closed when it first reaches QA Backlog (or, without QA stages, when Bitrix24 closes it).
Open tasks	Pending tasks: behind QA Backlog and not on hold. Department = the assignee's department. Unassigned: those of them nobody has picked up yet (the placeholder assignee); click to list them. Click any count to list those tasks below.
Overdue	Open tasks whose deadline has passed. "Over 30 days" = more than 30 days late.

Closed	Tasks closed in the period (first QA Backlog, else the Bitrix24 closed date). Clean-ups of 30+ tasks closed in one project on one day are left out.
On-time	Of the tasks closed in the period that had a deadline, the share closed on or before it.
Projects	Every project active in Bitrix24, all departments (only the Project filter narrows it) = Active + Silent + Hold, the same rule as the Development Projects tile. Hold: every unfinished task is in On Hold. Active: open tasks and a task changed or moved in the last 30 days (bulk changes left out). Silent: the rest (no open task, or no activity for 30 days). Click the tile or a part to list those projects in Project health.
Tasks in hand	Open tasks whose deadline is still ahead (IST), by when they are planned: tomorrow, the rest of this week, the rest of this month, next week, next month. The parts overlap (tomorrow is also in the rest of the week), so they do not add up. Overdue and no-deadline tasks are counted in their own tiles. Click the tile for the planner: day, week or month columns per person (with the projects they work on) or per project (with who works on it), overdue first in red.
Tasks in hand by assignee	Open tasks with the deadline ahead, per assignee or project. The chart shows the window picked above it (All, Tomorrow, Rest of week, Rest of month, Next week, Next month); the table shows every window. A bar or count opens those tasks; a name sets the filter.
No deadline	Open tasks without a deadline: they cannot be overdue or planned.
Insights	Findings worked out from the same numbers. Click one to see its tasks. Start here each morning. Click the title to focus it in the centre; drag ⠿ at the top to move it.
Project health	One row per project, worst first. Red: over 25 % of open tasks overdue (at least 3), or a task over 30 days late. Amber: any overdue task, or silent. Green: neither.
Overdue breakdown	Open tasks past their deadline, by how many days late, per project and per person.
Workload	Open project tasks per person: overdue, due in the next 10 working days, due later, no deadline.
People	Per person: tasks closed in the period (vs the one before), on-time %, open and overdue now, QA send-backs on closed tasks, and closed tasks over the last 8 periods.

Activity	Busiest projects of the last 7 days: new tasks, bugs raised, stage moves and comments (ranked by new×2 + bugs×3 + moves + comments). Silent projects below.
All tasks	Every number on this tab opens its tasks here. Edit in place, bulk edit and Excel export work as on the other tabs.
