Nural Pulse

Module guide

Every page you can open, module by module: what every tile, card and list shows and how to use it.

For Product owners

NURALTECH · internal · Powered by Bitrix24 and Nural

21 October 2026

Contents

01	On every page	The parts every page shares
02	KPI	Management overview
03	Development	Tasks, issues and deadlines
04	QA	Bugs, feedback, testing and retesting
05	Daily update	Plan, wrap up, post to Slack
06	Insights	What is holding us back
07	Workflow	Stages and what they count as
08	Project types	Projects grouped by their boards
09	Feedback	Issues and ideas, with attachments
10	Documents	The PDF guides
11	FAQs	Common questions
12	Definitions	The rules behind the numbers

01 On every page


The parts every page shares

PART	WHAT IT DOES
One number, two places	The same data point can show a different number on two pages, because each counts within its own department or group: Development counts the Development department, QA the bugs and feedback, KPI the whole company, Insights the period you chose. Click any number to see exactly which tasks it counts.
The menu	Every page, by module (Dashboard, Insights, Employees, Integration). The module of the page you are on is highlighted and open; click another module to open it. Drag ⠿ to put modules in your order, and pages within their own module. Hover the icons to open the menu; click ☰ to pin it open.
Filters	Project, assignee, tag and date range narrow every number on the tab. Reset filters clears them. The "i" icons say exactly what each number counts.
Alerts	The bell counts overdue tasks and tasks stuck over 5 days in one stage. Click it for the list and jump to the tasks.
Live	Live means changes in Bitrix24 reach the dashboard within seconds; numbers refresh by themselves. Offline means the connection dropped and it is reconnecting.
Page tools	On the right: Customise (choose the tiles and cards to show), the guided tour of this page, the PDF guides, Export page (every data point on the page as one Excel workbook or PDF), reading tours aloud, and resetting the layout. Hover any icon for its name. Each data point also has a small toolbar on hover: ⠿ to move it, ? to explain it, the eye to hide it. Tables have Columns (choose and order them) and ⠿ on each row to put rows in your own order.
Your profile	Your name and role, the theme (Light, Dark, System), live-update toasts, Reset layout, this tour (replay, voice on or off) and Sign out. You are signed out 3 days after signing in.

02 KPI

Management overview

The management overview of every project and department. Period: Day, Week or Month; "closed" and "on-time" compare with the period before.

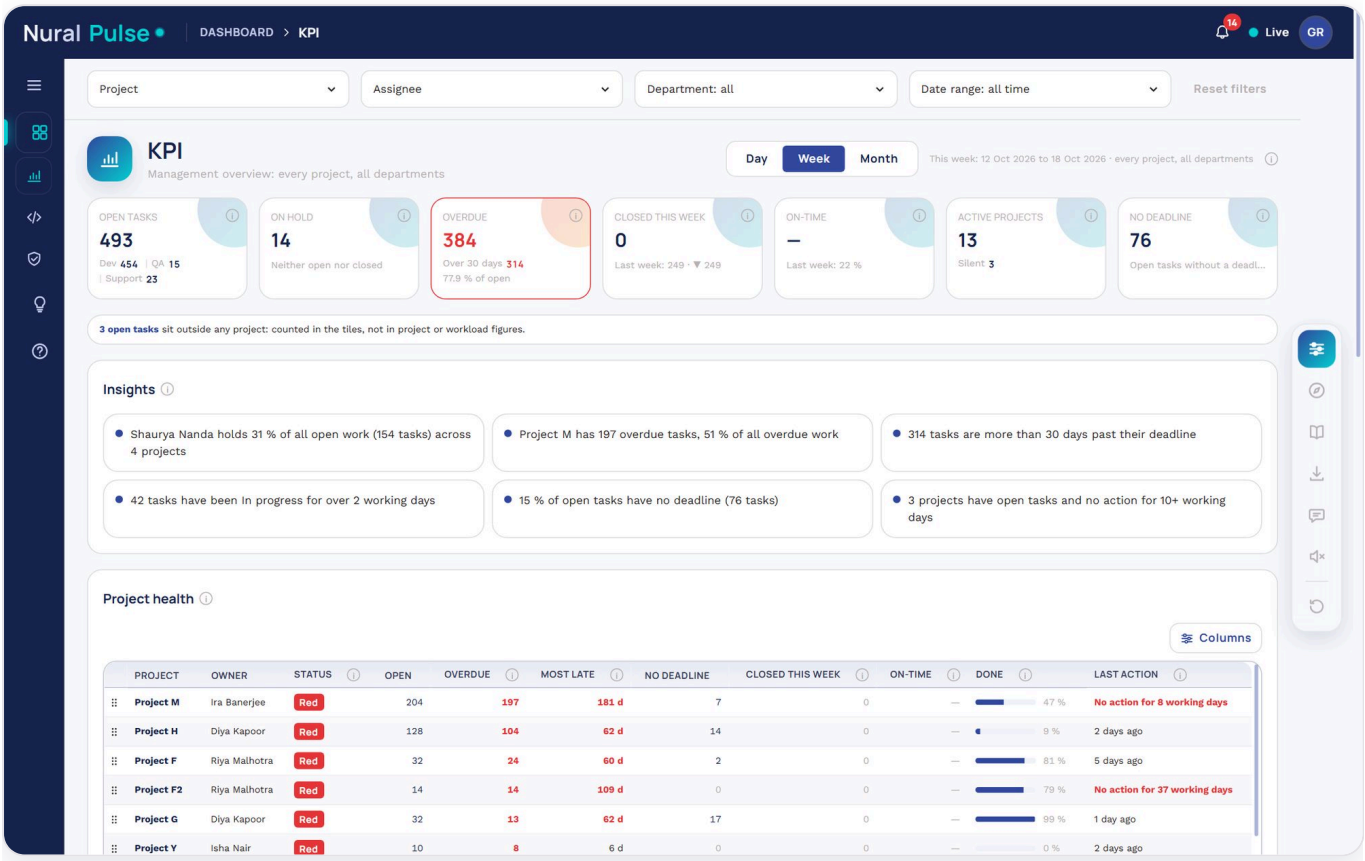

KPI, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Day, Week or Month	The period changes only the glowing data points: Closed, On-time, Project health (closed in the period) and People (delivered in the period), each compared with the period before. Open, On hold, Overdue, Projects and No deadline are counted as of now, whatever the period. Every task in every project, all departments. A task is closed when it first reaches QA Backlog (or, without QA stages, when Bitrix24 closes it).
Open tasks	Pending tasks: behind QA Backlog and not on hold. Department = the assignee's department. Unassigned: those of them nobody has picked up yet (the placeholder assignee); click to list them. Click any count to list those tasks below.
Overdue	Open tasks whose deadline has passed. "Over 30 days" = more than 30 days late.


Closed	Tasks closed in the period (first QA Backlog, else the Bitrix24 closed date). Clean-ups of 30+ tasks closed in one project on one day are left out.
On-time	Of the tasks closed in the period that had a deadline, the share closed on or before it.
Projects	Every project active in Bitrix24, all departments (only the Project filter narrows it) = Active + Silent + Hold, the same rule as the Development Projects tile. Hold: every unfinished task is in On Hold. Active: open tasks and a task changed or moved in the last 30 days (bulk changes left out). Silent: the rest (no open task, or no activity for 30 days). Click the tile or a part to list those projects in Project health.
Tasks in hand	Open tasks whose deadline is still ahead (IST), by when they are planned: tomorrow, the rest of this week, the rest of this month, next week, next month. The parts overlap (tomorrow is also in the rest of the week), so they do not add up. Overdue and no-deadline tasks are counted in their own tiles. Click the tile for the planner: day, week or month columns per person (with the projects they work on) or per project (with who works on it), overdue first in red.
Tasks in hand by assignee	Open tasks with the deadline ahead, per assignee or project. The chart shows the window picked above it (All, Tomorrow, Rest of week, Rest of month, Next week, Next month); the table shows every window. A bar or count opens those tasks; a name sets the filter.
No deadline	Open tasks without a deadline: they cannot be overdue or planned.
Insights	Findings worked out from the same numbers. Click one to see its tasks. Start here each morning. Click the title to focus it in the centre; drag ⠿ at the top to move it.
Project health	One row per project, worst first. Red: over 25 % of open tasks overdue (at least 3), or a task over 30 days late. Amber: any overdue task, or silent. Green: neither.
Overdue breakdown	Open tasks past their deadline, by how many days late, per project and per person.
Workload	Open project tasks per person: overdue, due in the next 10 working days, due later, no deadline.
People	Per person: tasks closed in the period (vs the one before), on-time %, open and overdue now, QA send-backs on closed tasks, and closed tasks over the last 8 periods.

Activity	Busiest projects of the last 7 days: new tasks, bugs raised, stage moves and comments (ranked by new×2 + bugs×3 + moves + comments). Silent projects below.
All tasks	Every number on this tab opens its tasks here. Edit in place, bulk edit and Excel export work as on the other tabs.

03 Development

Tasks, issues and deadlines

The Development department's tasks and issues. The All / Dev / Issues switch at the top steers every number.

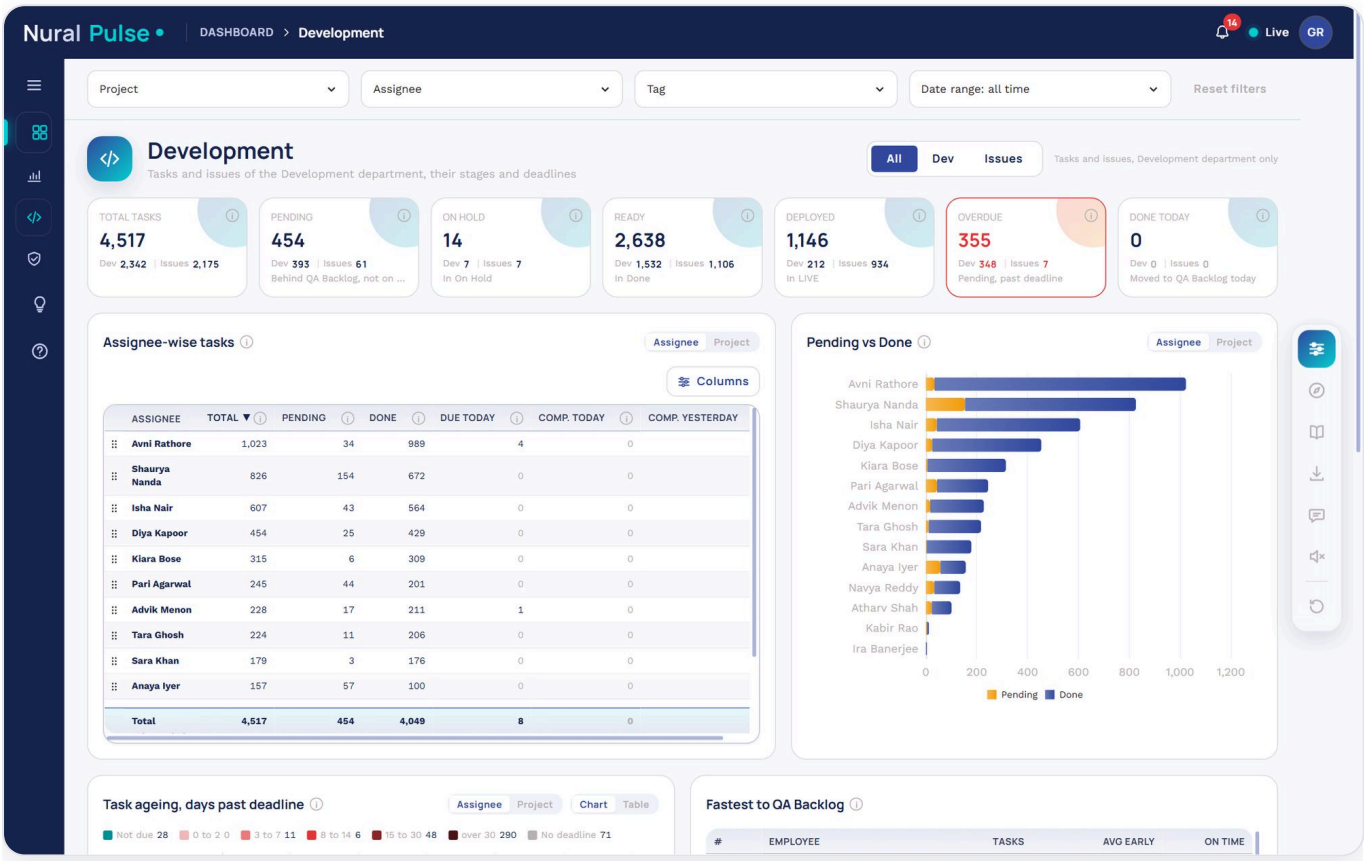

Development, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
All, Dev or Issues	Development department only. Dev = development tasks, Issues = bugs and feedback, All = both. It changes every tile, card and list on this page (they glow now).
Projects	Every project active in Bitrix24 whose owner is in the Development or QA Testing department, or a PM (fixed: the switch and filters do not change it; only the Project filter narrows it) = Active + Silent + Hold. Hold: every unfinished task is in On Hold. Active: open tasks and a task changed or moved in the last 30 days (bulk changes left out). Silent: the rest (no open task, or no activity for 30 days). Click for Projects at work, most active this week first, then the earliest deadline: open a project for who works on it. Its Day / Week / Month switch sets Done (previous period), Overdue (this period) and Spill (previous period).

Total	All tasks in the filters for the switch (Dev, Issues or both), Development department only. Under the number: the split into Dev and Issues (or Bug and Feedback). Click any count to list those tasks below.
Pending	Behind QA Backlog and not on hold: To do, In progress, Pushed to Master, Merged to Development, Pending for QA, Issue Raised. A testing or re-testing task in Issue Raised is not pending. Unassigned: those of them nobody has picked up yet (the placeholder assignee); click to list them. Click any count to list those tasks below.
On hold	In On Hold: neither pending nor completed. Pending + completed + on hold = total.
Ready to deploy	In the Done stage, ready to go live. Then Deployed: in the LIVE stage.
Overdue	Pending, not On Hold, and the deadline has passed. The first number to act on each day.
Done today	Reached QA Backlog for the first time today (IST).
Tasks in hand	Pending tasks (behind QA Backlog, not on hold) whose deadline is still ahead (IST). Under it, when they are planned: tomorrow, the rest of this week, the rest of this month, next week, next month. The parts overlap (tomorrow is also in the rest of the week), so they do not add up. Overdue and no-deadline tasks are not in hand. Click the tile for the planner: day, week or month columns per person (with the projects they work on) or per project (with who works on it), overdue first in red.
Tasks in hand by assignee	Pending tasks with the deadline ahead, per assignee or project. The chart shows the window picked above it (All, Tomorrow, Rest of week, Rest of month, Next week, Next month); the table shows every window. A bar or count opens those tasks; a name sets the filter.
Per person or project	Per person or project. Done = sent to QA (QA Backlog to LIVE). Comp. today = reached QA Backlog today. Switch Assignee / Project at the top. Every count opens its tasks. Click the title to focus it in the centre; drag ⠿ at the top to move it.
Pending vs Done	Pending vs completed (QA Backlog, In QA, Done, LIVE) per person or project, top 15 by total. Tooltip splits Dev / Issues (Bug / Feedback on Issues). Click a bar to open those tasks.
Task ageing	Open tasks by days past deadline. On Hold counts here but not as Overdue. The darker the red, the later. Chart or Table at the top.
On-time ranking	Tasks sent to QA with a deadline. Ranked by on-time %, then average days early. Fewer than 3: not ranked.
Tasks by stage	Tasks per Kanban stage; the colour bar shows each stage total. The red part of a cell is overdue. Click a cell for those tasks.

Task lists	Due today, Overdue, All tasks and Alert details open here. Clicking any number above opens All tasks narrowed to it. In a list: click a cell to change stage, status or tags (and more for leads), tick rows for bulk edit, and export to Excel.


Task lists

Due today, Overdue, All tasks (follows the last number you clicked) and Alert details. Each list sorts, edits in place, bulk edits, pages and exports to Excel.

04 QA

Bugs, feedback, testing and retesting

Bugs and feedback (tasks tagged bug or feedback), testing work and the retest queue. The Bug or Feedback filter narrows the page.

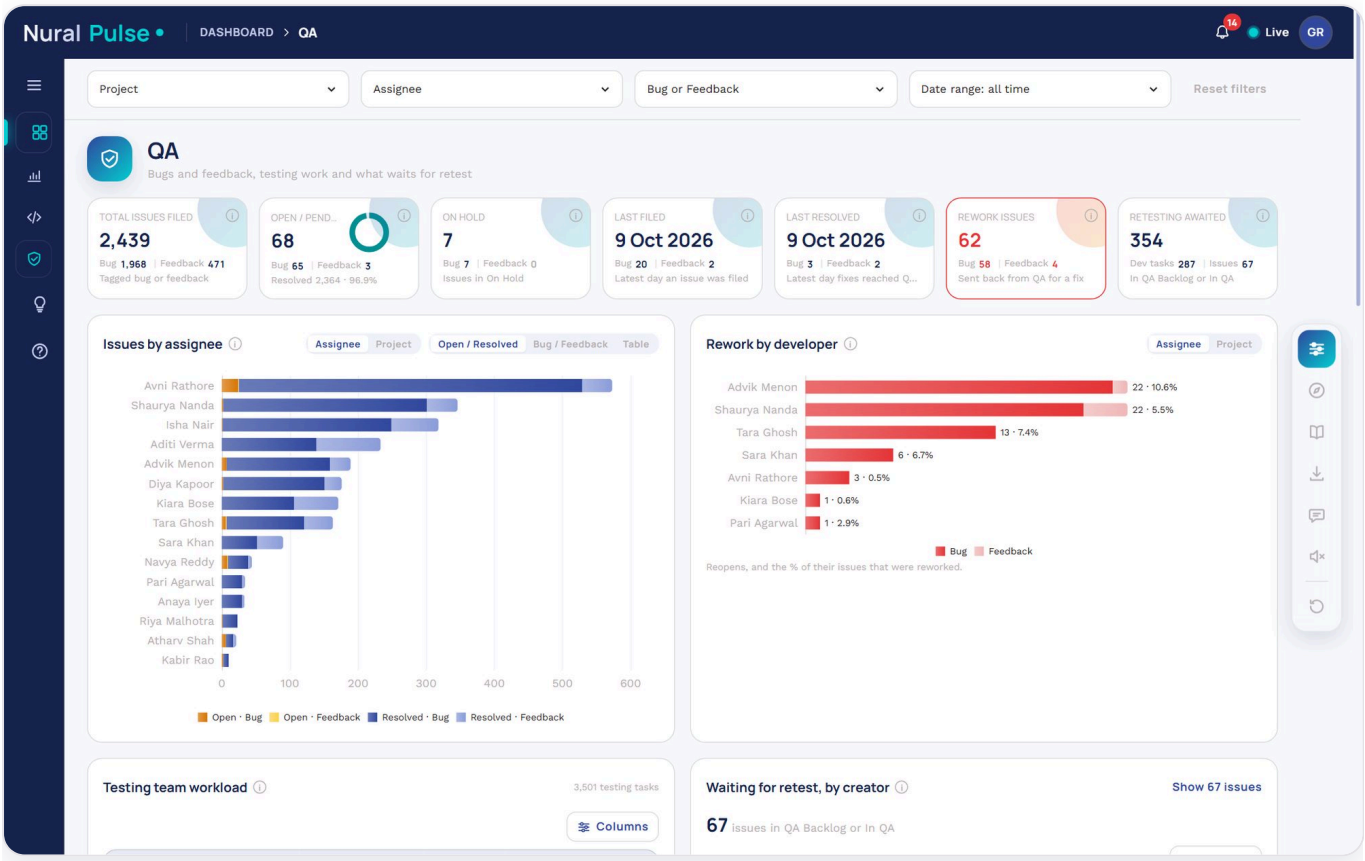

QA, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Issues filed	Every task tagged bug or feedback in the filters, whoever it is assigned to. Bug and Feedback under the number. Click any count to list those tasks below.
Tasks in hand	The QA Testing team's pending testing tasks whose deadline is still ahead (IST), by when they are planned: tomorrow, the rest of this week, the rest of this month, next week, next month. The parts overlap, so they do not add up. Click the tile for the planner: day, week or month columns per person (with the projects they work on) or per project (with who works on it), overdue first in red.
Tasks in hand by assignee	The testing team's pending tasks with the deadline ahead, per assignee or project. The chart shows the window picked above it; the table shows every window. A bar or count opens those tasks; a name sets the filter.

Open / pending	Open = pending: any stage behind QA Backlog except On Hold (Issue Raised included). Resolved = QA Backlog, In QA, Done or LIVE. On Hold is its own tile. The ring shows the resolved %. Unassigned: those of them nobody has picked up yet (the placeholder assignee); click to list them. Click the tile for the open issues by project: open a project for who filed them, and a creator for who has them, each with Pending and Overdue.
On hold	In On Hold: neither pending nor completed. Pending + completed + on hold = total.
Last filed and resolved	Latest day an issue was created, and how many that day. Click for that day by project: open a project for who filed its issues (bug and feedback), and a creator for who they went to. Next to it, Last resolved: Latest day issues were pushed to QA Backlog (a fix handed to QA), and how many that day.
Rework	Issues QA sent back after testing: from QA Backlog, In QA or Done to Issue Raised, To do or In progress. Stage flow only.
Retesting awaited	Every task waiting for QA: in QA Backlog or In QA, split into dev tasks and issues (bug or feedback). The QA team's queue.
Issues by person	Open vs resolved, each split into bug and feedback (or the reverse), per person or project. Table: the assignee-wise table. Click the title to focus it in the centre; drag ⠿ at the top to move it.
Rework by developer	QA send-backs per person or project, split into bug and feedback, and the % of their issues sent back. First Issue Raised to To do is not counted.
Testing tasks	Tasks tagged testing or re-testing, or assigned to QA Testing. Late = pending past deadline. A testing or re-testing task in Issue Raised is "Issue raised": not pending, never late.
Waiting for retest	Issues in QA Backlog or In QA, by who filed them. Oldest = days waiting.
Retest queue by person	Tasks and issues in QA Backlog and In QA per assignee or project. Every number opens its tasks.
Issue trend	Last 7 days (IST): bugs and feedback filed (created, light) and resolved (pushed to QA Backlog that day, dark). Pick one assignee or project, or see all. Click a point for that day's issues.
Issue ageing	Open issues by days past deadline (same as task ageing). On Hold counts here.
Issues by stage	Issues per stage and person (or project). Red = overdue part. Bug / Feedback narrows it.

Issue lists	Latest filed, Latest resolved and All issues. Any number above opens All issues narrowed to it. Edit in place, bulk edit and Excel export work as on Development.

Issue lists

Latest filed, Latest resolved and All issues (follows the last number you clicked), with the same editing and export as on Development.

05 Daily update

Plan, wrap up, post to Slack

Your morning plan and evening wrap-up, opened from the Daily update icon in the page tools and posted to the daily work update group on Slack. The page lists your last 30 days.

Every data point


DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Plan your day	Open it from the Daily update icon in the dock: what carries over from your last plan (still pending or WIP), your overdue and due-today tasks, upcoming ones you can take on early, and those with no deadline (plan one and its deadline is set to today when you post). Change any task right in its row (stage, status, tags…), keep, remove or add, write a note and post it to the daily work update group on Slack. You can open it all day to see and change your plan.
Wrap up your day	In the evening from the same icon, or when you sign out, your plan comes back with each task Pending, WIP, Done or On hold (from its stage). Report one as Done to complete it in Bitrix24, add tasks you finished ahead, and work outside the plan becomes a Bitrix24 task assigned to you. Then it goes to the same Slack thread.
My last 30 days	Each day you posted: tasks planned, done, WIP and outside the plan. Open the Daily update any time from its icon in the dock on the right.

06

Insights

What is holding us back

Findings from Bitrix24 and dashboard data, ranked: causes first (projects pulling people away), then releases at risk, lagging projects, overload, lagging people and people with room. Period: 7, 14 or 30 days. Every finding opens its tasks.

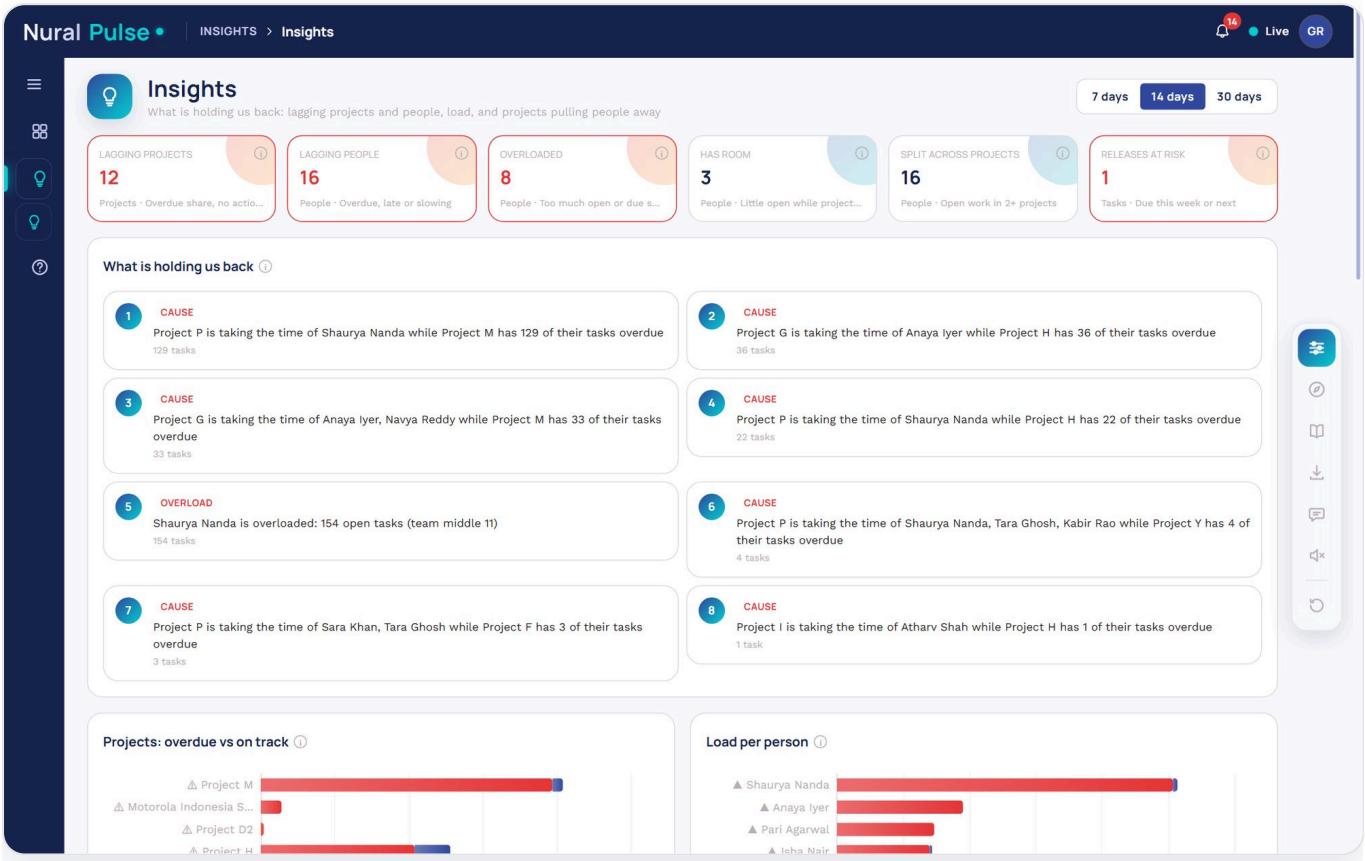

Insights, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Insights	What is holding us back, worked out from Bitrix24 data. 7, 14 or 30 days sets how far back activity is looked at: it changes the glowing data points (lagging projects and people, has room, the findings, projects, load and pulls). Overload, people split across projects and the release plan are counted as of now.
At a glance	Lagging projects and people, the overloaded, those with room to help, people split across projects and releases at risk. Click a tile for the projects or people it counts, with why each is there; click one of them for its tasks.
What is holding us back	The findings ranked, causes first: a project taking people's time while another project's tasks go overdue, then lagging projects and people, overload, people with room and risky releases. Click one for its tasks.

Projects	Open tasks per project with the overdue part; ⚠ marks a lagging project. Hover for why; click for the tasks.
Load	Open tasks per person: overdue, due in the next 5 working days and the rest. ▲ overloaded, ▽ has room to take tasks over.
Projects pulling people away	Who has open work in several projects, how much they do in each, and which project is taking their time while another goes overdue.
Release plan	Tasks due this week and next with their planned date, stage and risk of slipping. Click a row for the task.
Leave and attendance	From Infowan once connected: leave, late arrivals and early leaving, and the tasks and projects they put at risk. Until then insights use Bitrix24 data.

The rules

FINDING	RULE
Lagging project	3+ overdue and 25 % or more of its open tasks; or no action for 10+ working days; or closing half or less of the period before.
Lagging person	3+ overdue and 30 % or more of their open tasks; or under 50 % on time; or closing half or less of the period before with 5+ open.
Overloaded	10+ open and twice the team median, or 8+ due in the next 5 working days.
Has room	2 or fewer open and closed while one of their projects has overdue work.
Pulling people away	One project takes 70 % or more of a person's actions while their tasks in another project are overdue.
Release risk	Open tasks due this week or next: high if overdue, or not started and due within 2 working days.

07 Workflow

Stages and what they count as

The stages a task moves through, in order: what each counts as (pending, on hold or completed), the part it plays, who works in it and the usual moves. Admins change it; every number follows.

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
How work flows	A task moves left to right through the Kanban stages to LIVE. Each lane is a department: the PM or team lead plans it (To do), Development builds it (In progress, Pushed to Master, Merged to Development, Pending for QA), QA tests it (QA Backlog, In QA, Done, or Issue Raised to send it back) and Release puts it live. Solid arrows are the usual moves, red dashed ones QA sending work back. The band underneath shows what each stage counts as. Click a stage for details.
One stage	What the stage means, who acts there, where it moves on to, the board column names that mean it, and which numbers on the dashboard it feeds.
Who does what	Each department and the stages where the next step is theirs.
Edit the workflow (admins)	Admins change the stages: order, names, departments, what each counts as, its roles, column names and arrows, and the rework rule. Once saved, every number on every page counts with it. Every version is kept and can be restored.

08 Project types

Projects grouped by their boards

Each project type with its rule (the stages its board must or must not have) and its projects. A board column the workflow does not know is outlined in red.

Every data point


DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Projects that differ	Most projects follow the full development flow to LIVE. Support desks, DevOps and personal projects use short boards (New › In progress › Finished), others skip the code or release stages. Their numbers follow the same rules, with fewer stages.
Projects by type	Each type with its rule and its projects. Every project shows its own columns and the stage each counts as; a column the workflow does not know is outlined in red. Admins set a project’s type by hand, map an unknown column to a stage, and edit the types.

09

Feedback

Issues and ideas, with attachments

Send feedback about the dashboard, a page, a project or a person (only those you can see), with up to 5 attachments of 8 MB: images (paste a screenshot with Ctrl+V), PDF, Excel, Word. My feedback shows what you sent and the reply. The Feedback inbox (admins, PM and team leads) reads everyone's, replies and exports to Excel.

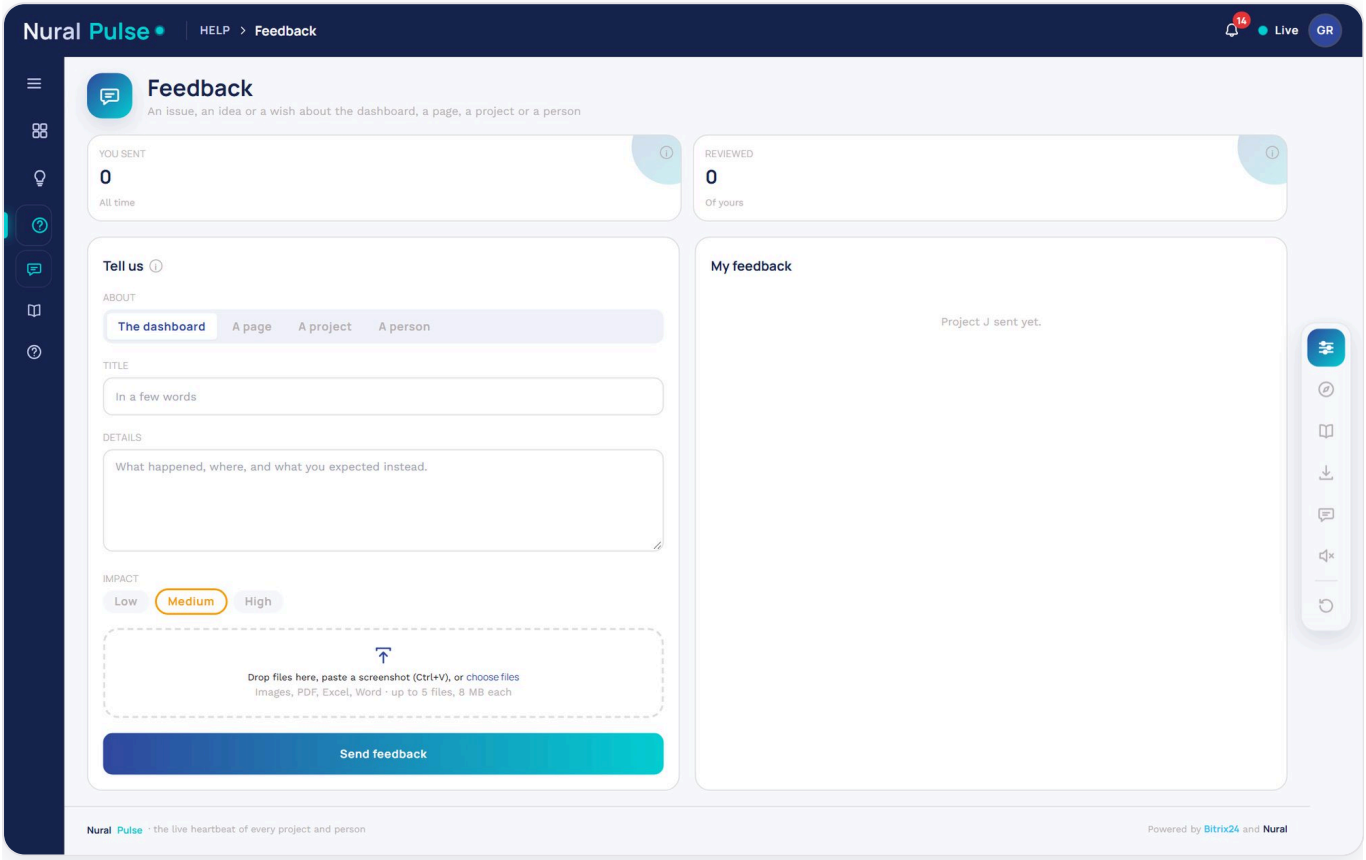

Feedback, as you see it (names replaced).


Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Tell us	An issue, an idea or a wish: about the dashboard, a page, a project or a person (only the ones you can see). Add screenshots (paste them with Ctrl+V), PDF, Excel or Word files, up to 5.
My feedback	What you sent, whether it has been reviewed, and the reply.

10 Documents

The PDF guides

The guides for your level of access: the whole dashboard (User guide, Module guide) and one short guide per page you can open.

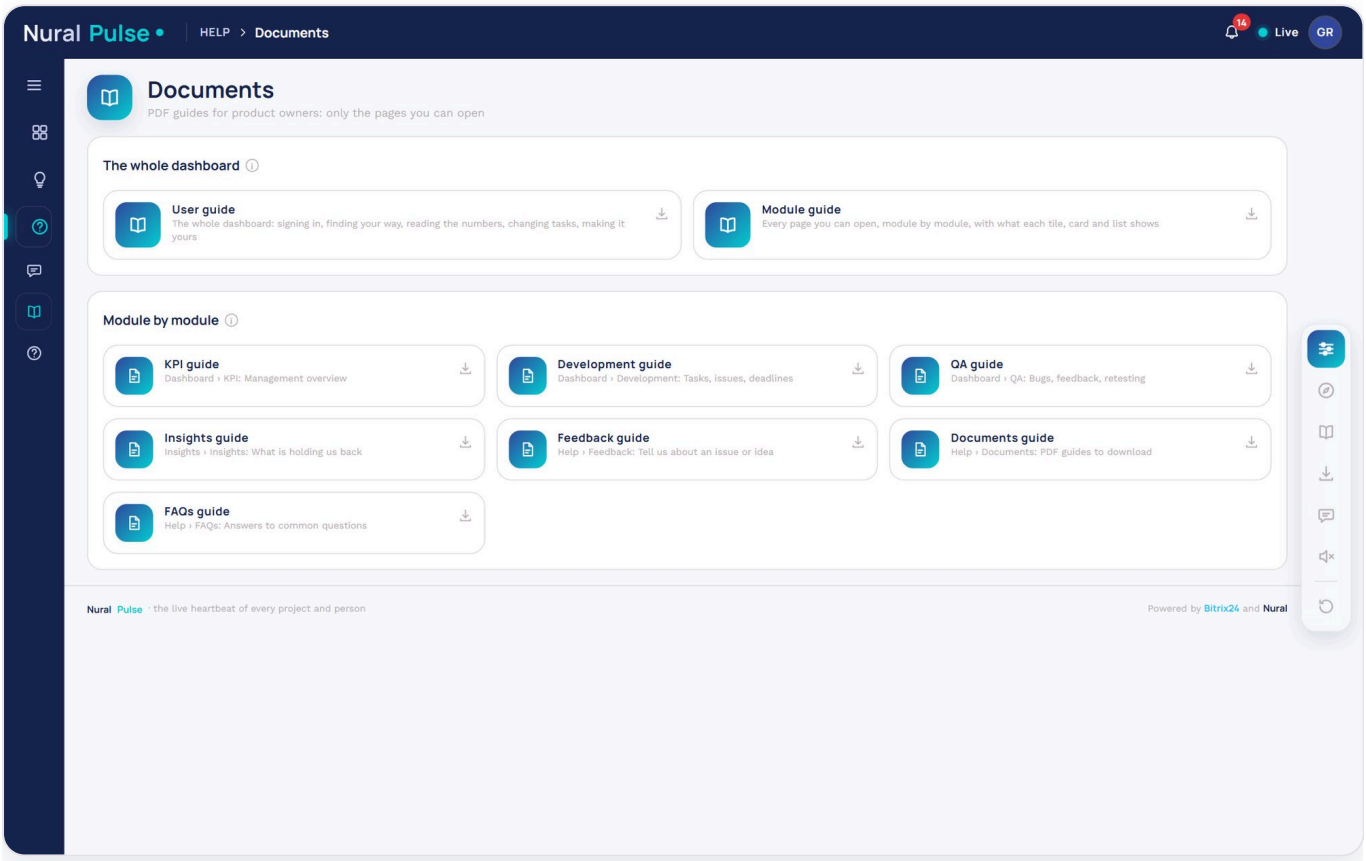

Documents, as you see it (names replaced).


Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Guides	PDF guides for your level of access: the whole dashboard, and module by module. Only the pages you can open are in them.

11 FAQs

Common questions

Answers by topic: the numbers, clicking and filtering, changing tasks, making it yours, access and sign-in, Insights and reports. Search at the top.

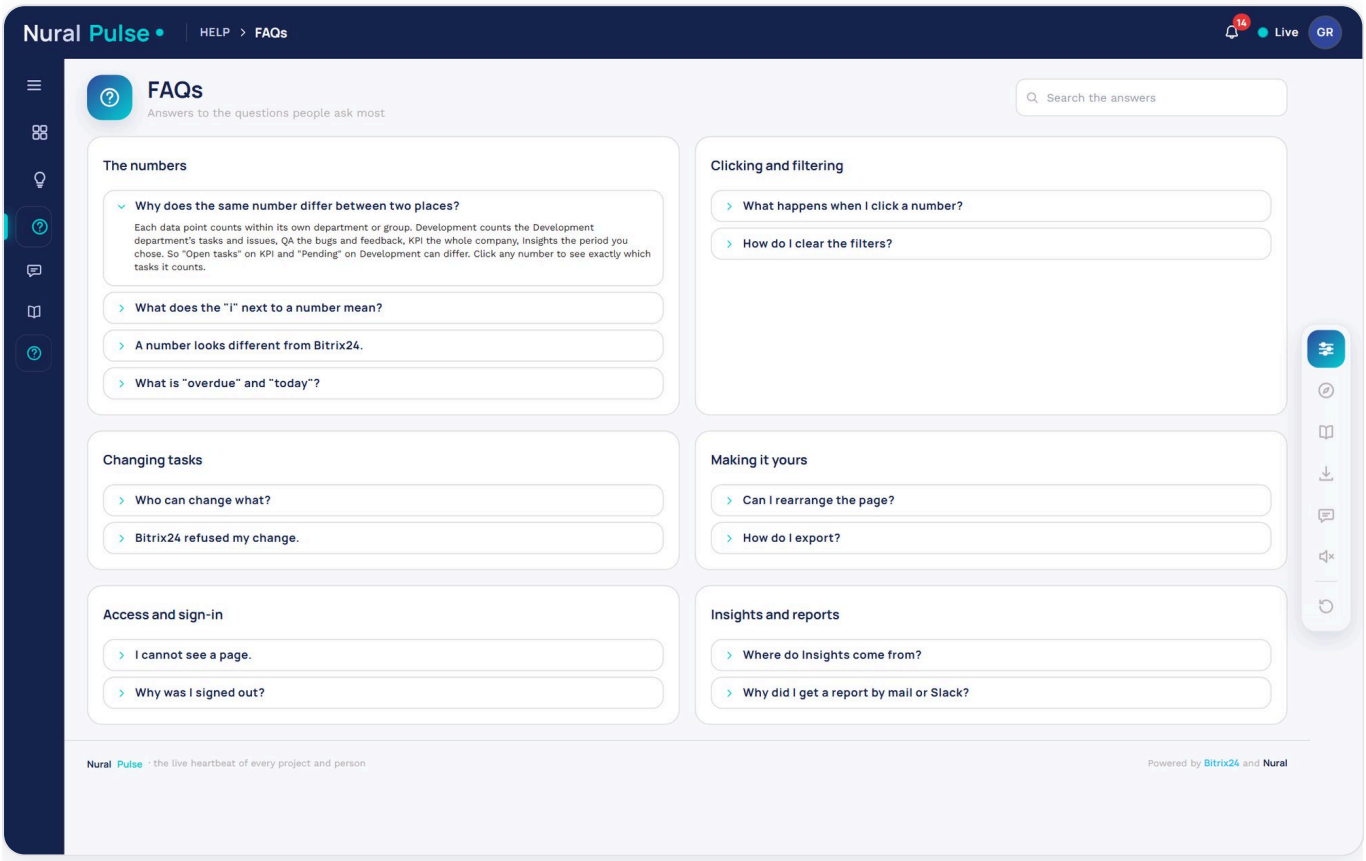

FAQs, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
FAQs	Answers to the questions people ask most, by topic. Search at the top.

12 Definitions

The rules behind the numbers

TERM	RULE
Pending	Behind QA Backlog and not on hold: To do, In progress, Pushed to Master, Merged to Development, Pending for QA, Issue Raised. A testing or re-testing task in Issue Raised is not pending. Unassigned: those of them nobody has picked up yet (the placeholder assignee); click to list them.
On hold	In On Hold: neither pending nor completed. Pending + completed + on hold = total.
Completed (done)	Completed: in QA Backlog, In QA, Done or LIVE.
Overdue	Pending, not On Hold, and the deadline has passed.
Done today	Reached QA Backlog for the first time today (IST).
Due today	Deadline is today (IST), in any stage except LIVE.
Rework	Issues QA sent back after testing: from QA Backlog, In QA or Done to Issue Raised, To do or In progress. Stage flow only.
Retesting awaited	Every task waiting for QA: in QA Backlog or In QA, split into dev tasks and issues (bug or feedback).
Testing tasks	Tasks tagged testing or re-testing, or assigned to QA Testing. Late = pending past deadline. A testing or re-testing task in Issue Raised is "Issue raised": not pending, never late.
Closed (KPI)	Tasks closed in the period (first QA Backlog, else the Bitrix24 closed date). Clean-ups of 30+ tasks closed in one project on one day are left out.
On-time (KPI)	Of the tasks closed in the period that had a deadline, the share closed on or before it.
Working time	Working time: Monday to Friday, 09:30 to 18:30 IST, public holidays excluded.
