Nural Pulse

Insights guide

What is holding us back. What the page shows and how to use it.

For Members


NURALTECH · internal · Powered by Bitrix24 and Nural

15 October 2026

01 Insights

What is holding us back

Findings from Bitrix24 and dashboard data, ranked: causes first (projects pulling people away), then releases at risk, lagging projects, overload, lagging people and people with room. Period: 7, 14 or 30 days. Every finding opens its tasks.

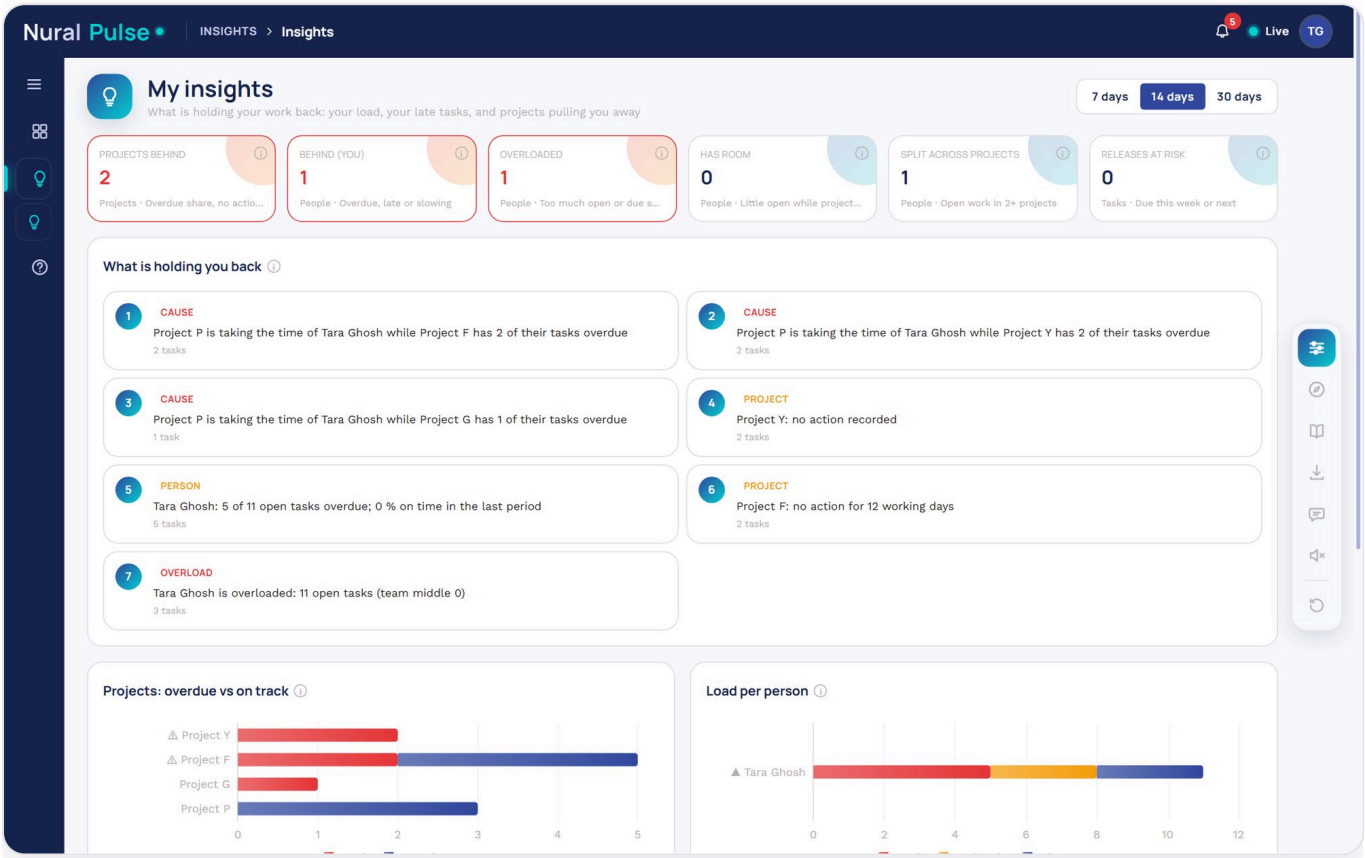

Insights, as you see it (names replaced).

Every data point

DATA POINT	WHAT IT SHOWS AND HOW TO USE IT
Insights	What is holding your work back. 7, 14 or 30 days sets how far back your activity is looked at: it changes the glowing data points; overload, split work and the release plan are as of now.
At a glance	Lagging projects and people, the overloaded, those with room to help, people split across projects and releases at risk. Click a tile for the projects or people it counts, with why each is there; click one of them for its tasks.
What is holding us back	Your findings ranked, causes first: a project taking your time while your tasks in another go overdue, then your late work and releases at risk. Click one for its tasks.

Projects	Open tasks per project with the overdue part; ⚠ marks a lagging project. Hover for why; click for the tasks.
Load	Open tasks per person: overdue, due in the next 5 working days and the rest. ▲ overloaded, ▽ has room to take tasks over.
Projects pulling people away	Who has open work in several projects, how much they do in each, and which project is taking their time while another goes overdue.
Release plan	Tasks due this week and next with their planned date, stage and risk of slipping. Click a row for the task.
Leave and attendance	From Infowan once connected: leave, late arrivals and early leaving, and the tasks and projects they put at risk. Until then insights use Bitrix24 data.

The rules

FINDING	RULE
Lagging project	3+ overdue and 25 % or more of its open tasks; or no action for 10+ working days; or closing half or less of the period before.
Lagging person	3+ overdue and 30 % or more of their open tasks; or under 50 % on time; or closing half or less of the period before with 5+ open.
Overloaded	10+ open and twice the team median, or 8+ due in the next 5 working days.
Has room	2 or fewer open and closed while one of their projects has overdue work.
Pulling people away	One project takes 70 % or more of a person's actions while their tasks in another project are overdue.
Release risk	Open tasks due this week or next: high if overdue, or not started and due within 2 working days.
