**Nural** Dev and QA Dashboard

# Insights guide

What is holding us back. What the page shows and how to use it.

For Support team


NURALTECH · internal

12 October 2026

# 01 Insights

What is holding us back

Findings from Bitrix24 and dashboard data, ranked: causes first (projects pulling people away), then releases at risk, lagging projects, overload, lagging people and people with room. Period: 7, 14 or 30 days. Every finding opens its tasks.

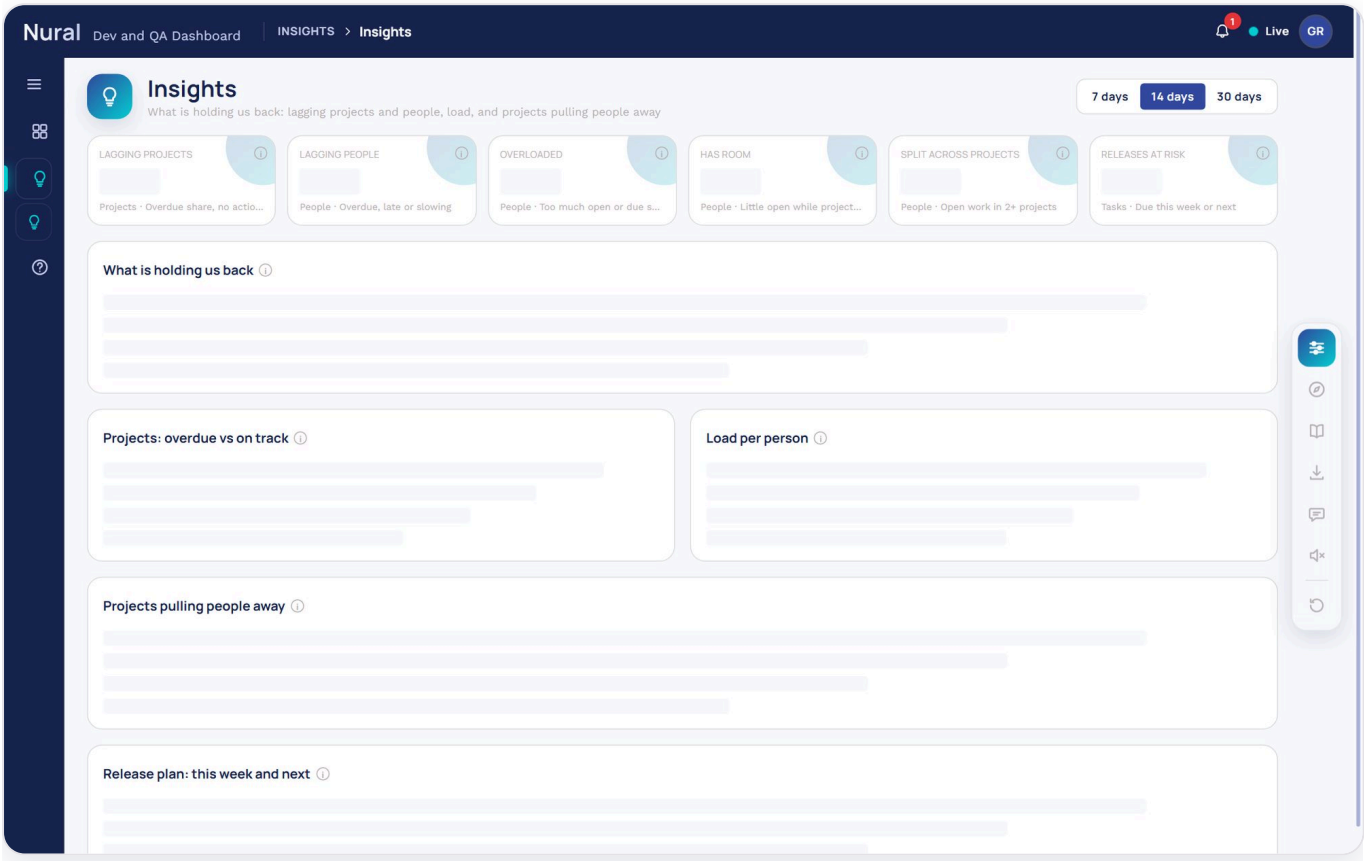


Insights, as you see it (names replaced).

## Every data point

| DATA POINT | WHAT IT SHOWS AND HOW TO USE IT |
|---|---|
| **Insights** | What is holding your work back. 7, 14 or 30 days sets how far back your activity is looked at: it changes the glowing data points; overload, split work and the release plan are as of now. |
| **At a glance** | Lagging projects and people, the overloaded, those with room to help, people split across projects and releases at risk. Click a tile for the projects or people it counts, with why each is there; click one of them for its tasks. |
| **What is holding us back** | Your findings ranked, causes first: a project taking your time while your tasks in another go overdue, then your late work and releases at risk. Click one for its tasks. |

| | |
|---|---|
| **Projects** | Open tasks per project with the overdue part; ⚠ marks a lagging project. Hover for why; click for the tasks. |
| **Load** | Open tasks per person: overdue, due in the next 5 working days and the rest. ▲ overloaded, ▽ has room to take tasks over. |
| **Projects pulling people away** | Who has open work in several projects, how much they do in each, and which project is taking their time while another goes overdue. |
| **Release plan** | Tasks due this week and next with their planned date, stage and risk of slipping. Click a row for the task. |
| **Leave and attendance** | From Infowan once connected: leave, late arrivals and early leaving, and the tasks and projects they put at risk. Until then insights use Bitrix24 data. |

## The rules

| FINDING | RULE |
|---|---|
| **Lagging project** | 3+ overdue and 25 % or more of its open tasks; or no action for 10+ working days; or closing half or less of the period before. |
| **Lagging person** | 3+ overdue and 30 % or more of their open tasks; or under 50 % on time; or closing half or less of the period before with 5+ open. |
| **Overloaded** | 10+ open and twice the team median, or 8+ due in the next 5 working days. |
| **Has room** | 2 or fewer open and closed while one of their projects has overdue work. |
| **Pulling people away** | One project takes 70 % or more of a person's actions while their tasks in another project are overdue. |
| **Release risk** | Open tasks due this week or next: high if overdue, or not started and due within 2 working days. |
